


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	% Complete
1		<b>BUDDY ATTICK PARK PARKING LOT RECONSTRUCTION PROJECT</b>	<b>131 days?</b>	<b>Fri 3/18/22</b>	<b>Fri 9/16/22</b>		<b>69%</b>
2	✓	NTP	0 days	Fri 3/18/22	Fri 3/18/22		100%
3	✓	PRE-CONSTRUCTION MEETING	0 days	Thu 3/31/22	Thu 3/31/22		100%
4	✓	STAKEOUT	0 days	Mon 4/11/22	Mon 4/11/22		100%
5	✓	Field meeting with inspector	0 days	Fri 4/22/22	Fri 4/22/22		100%
6		<b>Construction</b>	<b>72 days?</b>	<b>Wed 4/13/22</b>	<b>Thu 7/21/22</b>		<b>69%</b>
7	✓	TREE REMOVAL / GENERAL CLEANING.	7 days	Wed 4/13/22	Thu 4/21/22		100%
8	✓	INSTALL CONSTRUCTION ENTRANCE AND E&S MEASURES PHASE I	3 days	Fri 4/22/22	Tue 4/26/22	7	100%
9	✓	INSTALL E&S MEASURES PHASE I	2 days	Wed 4/27/22	Thu 4/28/22	8	100%
10	✓	EXCAVATION TO BIORETENTION & PLANTING AREAS PHASE I (PLANTING AREA CURB & BIO)	5 days	Fri 4/29/22	Thu 5/5/22	9	100%
11		<b>RAIN DAY (NO WORK)</b>	<b>1 day</b>	<b>Fri 5/6/22</b>	<b>Fri 5/6/22</b>	10	0%
12	✓	FURNISH AND INSTALL CURB PHASE I (PLANTING AREA)	4 days	Mon 5/9/22	Thu 5/12/22	11	100%
13		<b>RAIN DAY NO WORK</b>	<b>2 days</b>	<b>Fri 5/13/22</b>	<b>Mon 5/16/22</b>	12	0%
14	✓	DEFORMING, PATCH ALONG CURB INSTALLED, PLANTING MEDIA BACKFILL.	3 days	Tue 5/17/22	Thu 5/19/22	13	100%
15	✓	EXCAVATION TO BIORETENTION AREAS PHASE I	2 days	Fri 5/20/22	Mon 5/23/22	14	100%
16		<b>RAIN DAY NO WORK</b>	<b>1 day</b>	<b>Tue 5/24/22</b>	<b>Tue 5/24/22</b>	15	0%
17		FULL DEPTH CHANGE ORDER 1	2 days	Wed 5/25/22	Thu 5/26/22	16	85%
18		<b>RAIN DAY NO WORK</b>	<b>1 day</b>	<b>Fri 5/27/22</b>	<b>Fri 5/27/22</b>	17	0%
19		<b>MEMORIAL DAY NO WORK</b>	<b>1 day</b>	<b>Mon 5/30/22</b>	<b>Mon 5/30/22</b>	18	0%
20		FULL DEPTH CHANGE ORDER 1	2 days	Tue 5/31/22	Wed 6/1/22	19	85%
21	✓	UNDERDRAIN INSTALLATION PHASE I AT 1 BIORETENTION	4 days	Thu 6/2/22	Tue 6/7/22	20	100%
22	✓	EXCAVATION TO BIORETENTION AREAS PHASE I (2 SMALL)	3 days	Wed 6/8/22	Fri 6/10/22	21	100%
23	✓	FURNISH AND INSTALL CURB & SIDEWALK PHASE I	1 day	Mon 6/13/22	Mon 6/13/22	22	100%
24		<b>RAIN DAY NO WORK</b>	<b>1 day</b>	<b>Tue 6/14/22</b>	<b>Tue 6/14/22</b>	23	0%
25	✓	FURNISH AND INSTALL CURB, SIDEWALK & BASES PHASE I	6 days	Wed 6/15/22	Wed 6/22/22	24	100%
26		<b>RAIN DAY NO WORK</b>	<b>1 day</b>	<b>Thu 6/23/22</b>	<b>Thu 6/23/22</b>	25	0%
27	✓	INSTALLATION OF BIORETENTION LAYERS PHASE I	2 days	Fri 6/24/22	Mon 6/27/22	26	100%
28	✓	EXCAVATION OF FULL DEPTH PHASE I	1 day	Fri 6/24/22	Fri 6/24/22	26	100%
29		<b>RAIN DAY (ONLY 1/2 DAY WORK)</b>	<b>1 day</b>	<b>Mon 6/27/22</b>	<b>Mon 6/27/22</b>	28	0%
30	✓	GRAVEL INSTALLATION AND ASPHALT BASE INSTALLATION PHASE I	4 days	Tue 6/28/22	Fri 7/1/22	29	100%
31		<b>4TH JULY HOLIDAY</b>	<b>1 day</b>	<b>Mon 7/4/22</b>	<b>Mon 7/4/22</b>	30	0%
32	✓	INSTALL CONSTRUCTION ENTRANCE AND E&S MEASURES PHASE II	1 day	Tue 7/5/22	Tue 7/5/22	31	100%
33	✓	INSTALL E&S MEASURES PHASE II	2 days	Wed 7/6/22	Thu 7/7/22	32	100%
34	✓	UNDERDRAIN INSTALLATION PHASE II	3 days	Fri 7/8/22	Tue 7/12/22	33	100%
35	✓	<b>CLEAN ALL WORK FROM HEAVY RAIN (7/12/22)</b>	<b>1 day</b>	<b>Wed 7/13/22</b>	<b>Wed 7/13/22</b>	34	100%
36	✓	UNDERDRAIN INSTALLATION PHASE II BIORETENTIONS	3 days	Thu 7/14/22	Mon 7/18/22	35	100%
37	✓	FURNISH AND INSTALL CURB & CONCRETE PHASE II	4 days	Tue 7/19/22	Fri 7/22/22	36	100%
38	✓	GRADING (EXCAVATION FULL DEPTH AREA) AND GRAVEL INSTALLATION PHASE II	3 days	Mon 7/25/22	Wed 7/27/22	37	100%
39		<b>ELEVATIONS REVISION B CPJ.</b>	<b>6 days</b>	<b>Thu 7/28/22</b>	<b>Thu 8/4/22</b>	38	<b>0%</b>
40	✓	EXCAVATION TO BIORETENTION AREAS PHASE II	2 days	Mon 8/8/22	Tue 8/9/22	39	100%
41	✓	FURNISH AND INSTALL CURB & CONCRETE PHASE II	7 days	Wed 8/10/22	Thu 8/18/22	40	100%
42	✓	UNDERDRAIN INSTALLATION PHASE II BACK FLEXIPAVE	4 days	Fri 8/19/22	Wed 8/24/22	41	100%
43	✓	PCO#3 ELECTRICAL CONDUIT INSTALLATION.	2 days	Thu 8/25/22	Fri 8/26/22	42	100%
44	✓	INSTALLATION OF BIORETENTION LAYERS & FLEXIPAVE UNDERDRAIN BACKFIELD PHASE II	2 days	Thu 8/25/22	Fri 8/26/22	42	100%
45		FULL DEPTH INSTALLATION ALONG DRIVE AREA BETWEEN DPW AND RECYCLE CENTER.	2 days	Mon 8/29/22	Tue 8/30/22	44	20%
46		PCO#4 FULL DEPTH REGARDING THE CHANGES IN LEVELS AND BASE ASPHALT INSTALLATION (FULL DEPTH AREA PHASE II)	2 days	Wed 8/31/22	Thu 9/1/22	45	0%
47		SWALE REMOVE AND REPLACE (EXTRA WORK APPROVED 8/29/22)	3 days	Wed 8/31/22	Fri 9/2/22	45	0%
48		INSTALLATION OF PAVERS PHASE II	5 days	Mon 8/29/22	Fri 9/2/22	44	0%
49		<b>5TH SEP HOLIDAY LABOR DAY</b>	<b>1 day</b>	<b>Mon 9/5/22</b>	<b>Mon 9/5/22</b>	48	0%
50		<b>FLEXIPAVE INSTALLATION PHASE II</b>	<b>2 days</b>	<b>Thu 9/8/22</b>	<b>Fri 9/9/22</b>	49	<b>0%</b>
51		LANDSCAPING PHASE I & PHASE II	2 days	Mon 9/12/22	Tue 9/13/22	50	0%
52		TOPPING ASPHALT PHASE I & PHASE II	1 day?	Wed 9/14/22	Wed 9/14/22	51	0%
53		STRIPING PHASE I & PHASE II	1 day?	Thu 9/15/22	Thu 9/15/22	52	0%
54		GENERAL CLEANING & FINAL STABILIZATION	2 days	Fri 9/16/22	Mon 9/19/22	53	0%
55		<b>Substantial completion</b>	<b>1 day</b>	<b>Tue 9/20/22</b>	<b>Tue 9/20/22</b>	54	<b>0%</b>
56		Final Acceptance	1 day	Tue 9/20/22	Tue 9/20/22	55	0%

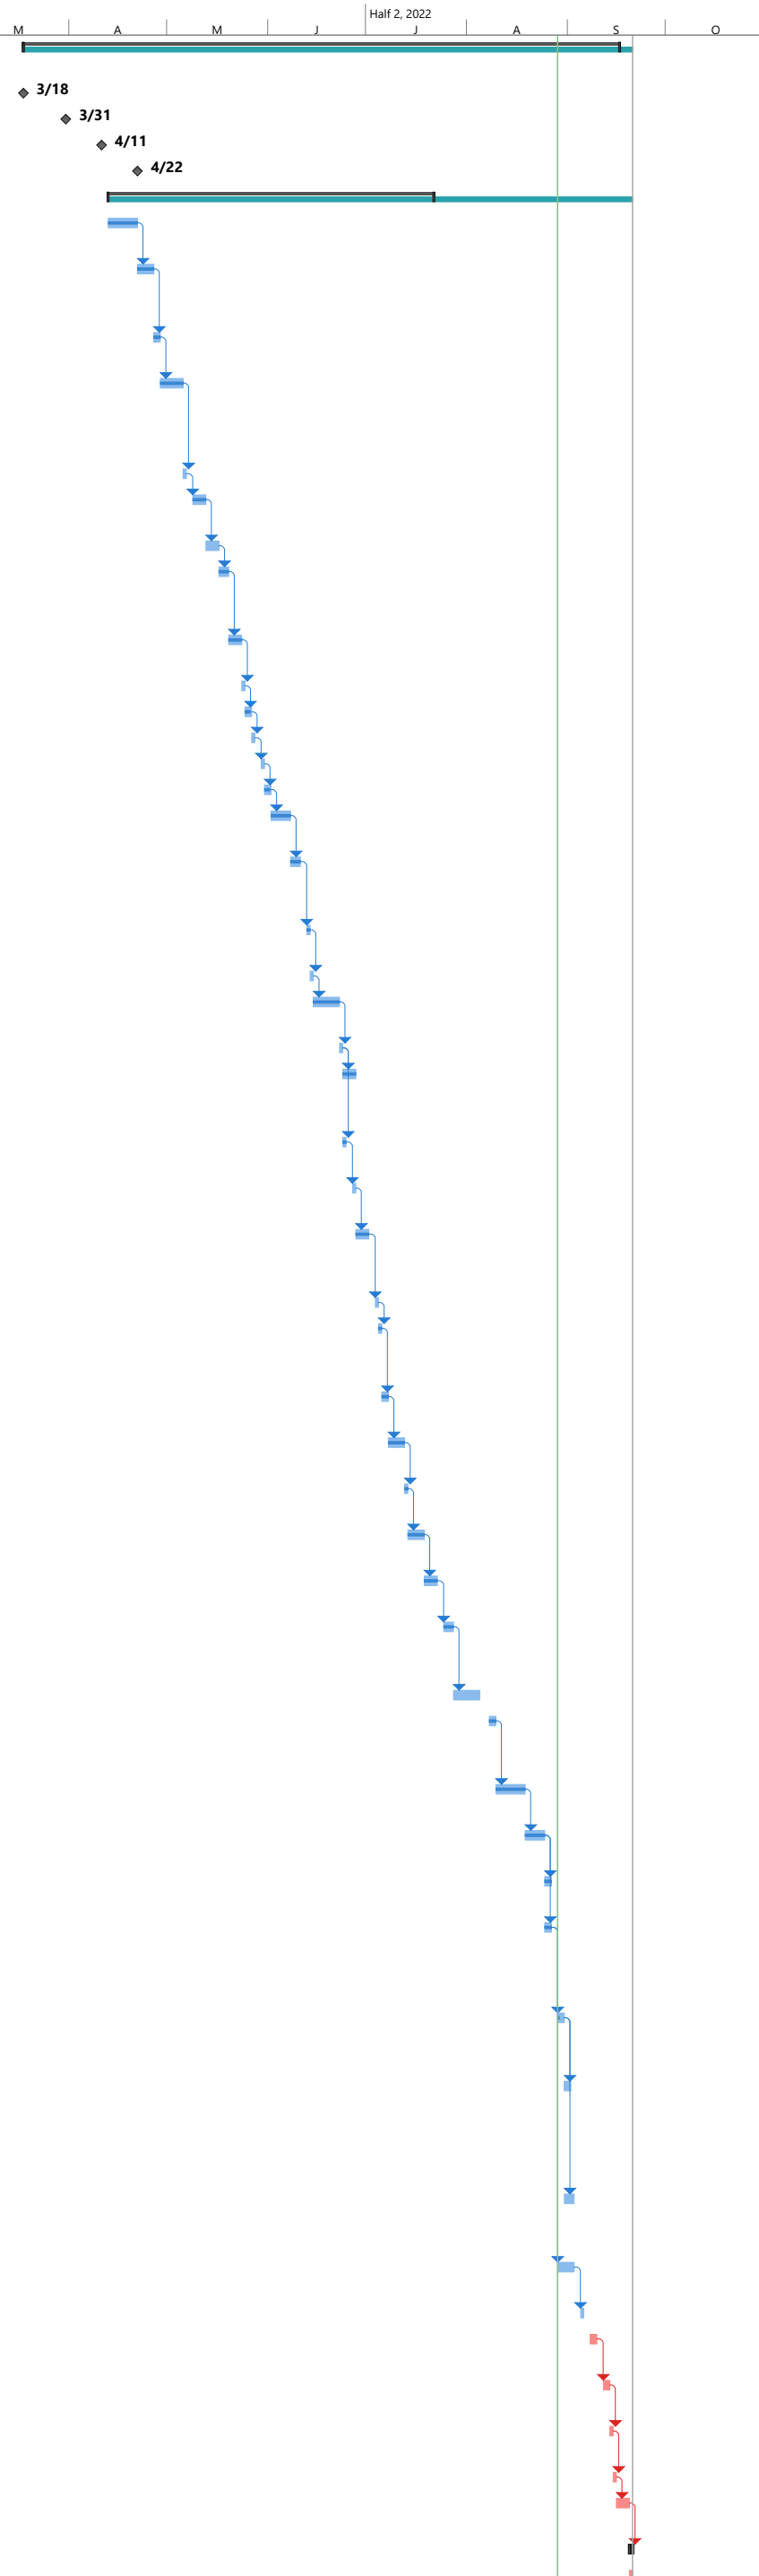

Project: Simple Project Plan Date: Mon 8/29/22	Task	Inactive Task	Manual Summary Rollup	External Milestone	Baseline Milestone
	Split	Inactive Milestone	Manual Summary	Deadline	Baseline Summary
	Milestone	Inactive Summary	Start-only	Critical	Progress
	Summary	Manual Task	Finish-only	Critical Split	Manual Progress
	Project Summary	Duration-only	External Tasks	Baseline	Manual Progress
