Greenbelt Station: WMATA Trail Project Schedule 04/10/2020

Dewberry

ID	Task Name	Start	Finish	Duration	Predecessors
1	**SWM Concept (DPIE)**	**Fri 9/21/18**	**Fri 6/7/19**	**186 days**	
2	DPIE Concept Approval	Fri 9/21/18	Fri 6/7/19	186 days	
3					
4	**ESC Concept (SCD)**	**Mon 6/10/19**	**Tue 11/12/19**	**112 days**	
5	SCD Concept Approval	Mon 6/10/19	Tue 11/12/19	112 days	
6					
7	**Mandatory Referral MR-1911A**	**Wed 7/17/19**	**Thu 4/9/20**	**192 days**	
8	MNCPPC MR Approval	Wed 7/17/19	Thu 4/9/20	38.4 wks	
9					
10	**DSP-04081-11/TCP-II Revision**	**Fri 3/13/20**	**Thu 6/18/20**	**70 days**	
11	MNCPPC review	Fri 3/13/20	Thu 5/14/20	9 wks	
12	Dewberry Address TCP-II Comments	Fri 5/15/20	Thu 5/28/20	2 wks	11
13	MNCPPC DSP/TCP Appr/Cert	Fri 5/29/20	Thu 6/18/20	3 wks	12
14					
15	**SWM Technical Approval (DPIE)**	**Wed 4/15/20**	**Wed 6/24/20**	**51 days**	
16	WMATA Application Approval	Wed 4/15/20	Wed 4/15/20	1 day	
17	Plan Approval (DPIE)	Thu 4/16/20	Wed 6/24/20	10 wks	6,8FF+3 wks
18					
19	**PGSCD Sediment Control Plans (Step 2)**	**Wed 4/8/20**	**Tue 5/26/20**	**35 days**	
20	Dewberry Address 2nd Review Comments	Wed 4/8/20	Tue 4/14/20	1 wk	
21	PGSCD Review/Approval	Wed 4/15/20	Tue 5/26/20	6 wks	20
22					
23	**PGSCD Sediment Control Plans (Step 3)**	**Thu 6/25/20**	**Wed 9/23/20**	**65 days**	
24	Plan Preparation	Thu 6/25/20	Wed 7/15/20	3 wks	17
25	PGSCD Review/Approval	Thu 7/16/20	Wed 9/23/20	10 wks	,21FS+2 wks
26					
27	**Topographic Survey (Parking lots, etc.)**	**Mon 5/11/20**	**Wed 7/8/20**	**43 days**	
28	JDAC Permit (WMATA)	Mon 5/11/20	Fri 6/19/20	6 wks	
29	Field Survey	Thu 6/25/20	Wed 7/8/20	2 wks	17,28
30					
31	**Trail Plans (City of Greenbelt)**	**Thu 7/9/20**	**Wed 12/23/20**	**120 days**	
32	Plan Preparation	Thu 7/9/20	Wed 9/2/20	8 wks	29,17
33	City of Greenbelt Review/Approval	Thu 9/3/20	Wed 9/30/20	4 wks	32
34	WMATA Review/Approval	Thu 9/3/20	Wed 12/23/20	16 wks	32
35					
36	**MDE Wetlands/Stream Crossing Permit**	**Wed 5/6/20**	**Wed 10/21/20**	**121 days**	
37	Impact Exhibit Prep/Coordination with Milt	Wed 5/6/20	Tue 5/26/20	3 wks	21FS-3 wks
38	MDE Permit Issuance	Thu 7/2/20	Wed 10/21/20	16 wks	',25FF+4 wks
39					
40	**Traffic Signal/Signage (Greenbelt, WMATA)**	**Thu 9/3/20**	**Wed 6/9/21**	**200 days**	
41	Plan Preparation	Thu 9/3/20	Wed 10/28/20	8 wks	32,29
42	City of Greenbelt/WMATA Approval	Thu 10/29/20	Wed 2/17/21	16 wks	41
43	Traffic Signal Building Permit	Thu 2/18/21	Wed 6/9/21	4 mons	42
44					
45	**Bridge/Boardwalk**	**Thu 9/3/20**	**Wed 2/10/21**	**115 days**	
46	Hydraulic Analysis/Report Preparation (MDE)	Thu 9/3/20	Wed 9/23/20	3 wks	32,37,29
47	MDE Review/Approval	Thu 9/24/20	Wed 11/18/20	8 wks	46
48	Building Permit (DPIE)	Thu 9/24/20	Wed 2/10/21	5 mons	38FS-1 mon
49					
50	**PDGPIE Grading, SWM Permit**	**Thu 9/24/20**	**Wed 11/25/20**	**45 days**	
51	Package Preparation	Thu 9/24/20	Wed 9/30/20	1 wk	8,17,25
52	PGDPIE Permit Issuance	Thu 10/1/20	Wed 11/25/20	8 wks	51
53					
54	**City of Greenbelt Permit Issuance**	**Thu 9/24/20**	**Wed 10/28/20**	**25 days**	
55	Package Preparation	Thu 9/24/20	Wed 9/30/20	1 wk	8,17,25
56	City of Greenbelt Permit Issuance	Thu 10/1/20	Wed 10/28/20	4 wks	55,25
57					
58	**WMATA Permit Issuance**	**Thu 9/24/20**	**Wed 12/9/20**	**55 days**	
59	Package Preparation	Thu 9/24/20	Wed 10/14/20	3 wks	8,17,25
60	WMATA Permit Issuance	Thu 10/15/20	Wed 12/9/20	8 wks	59

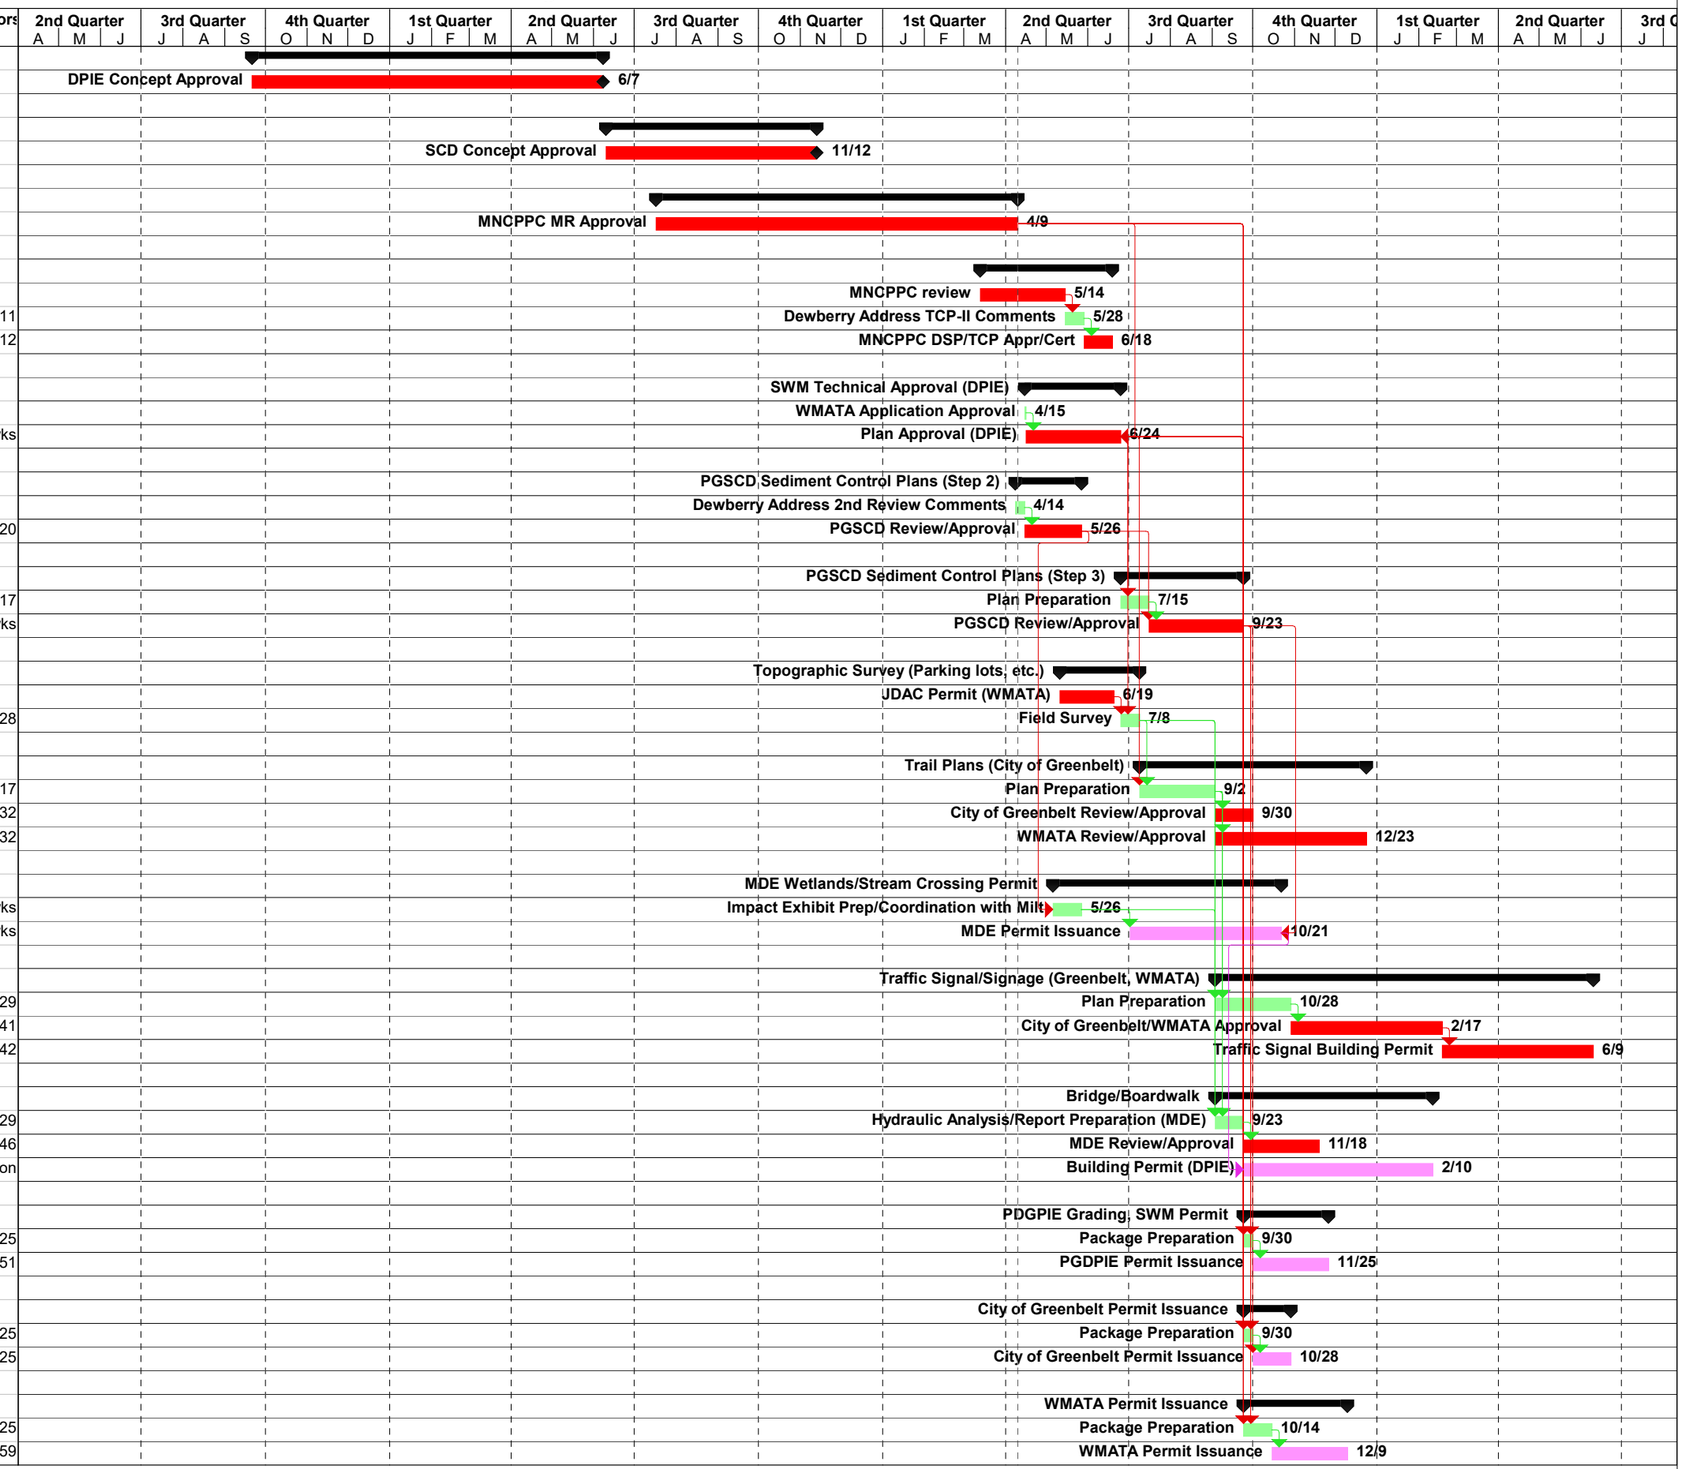

Schedules and dates included herein or otherwise communicated to Client are advisory only and cannot be guaranteed. Dewberry cannot be responsible or liable for damages or injuries caused by their use by Client in business plans or otherwise.
